



Installation

Client site:	Easystorage Gotham
Conducted on:	2026-03-29
Number of Cameras:	
System:	IP System
Equipment used:	

Number of cameras:


Description of works:

Installed a new network cabinet and completed the installation and commissioning of one horn speaker and three ColorVu cameras. All equipment was securely mounted within the cabinet, with power and data connections properly terminated and organised. Devices were configured and integrated into the network infrastructure, followed by full system testing to verify clear audio output from the horn speaker and stable live video feeds from all cameras. System was successfully onboarded to DSOC, with remote access and monitoring confirmed. Installation completed to operational standards with all components fully functional.

Work Image 1

Work Image 2


Work Image 3

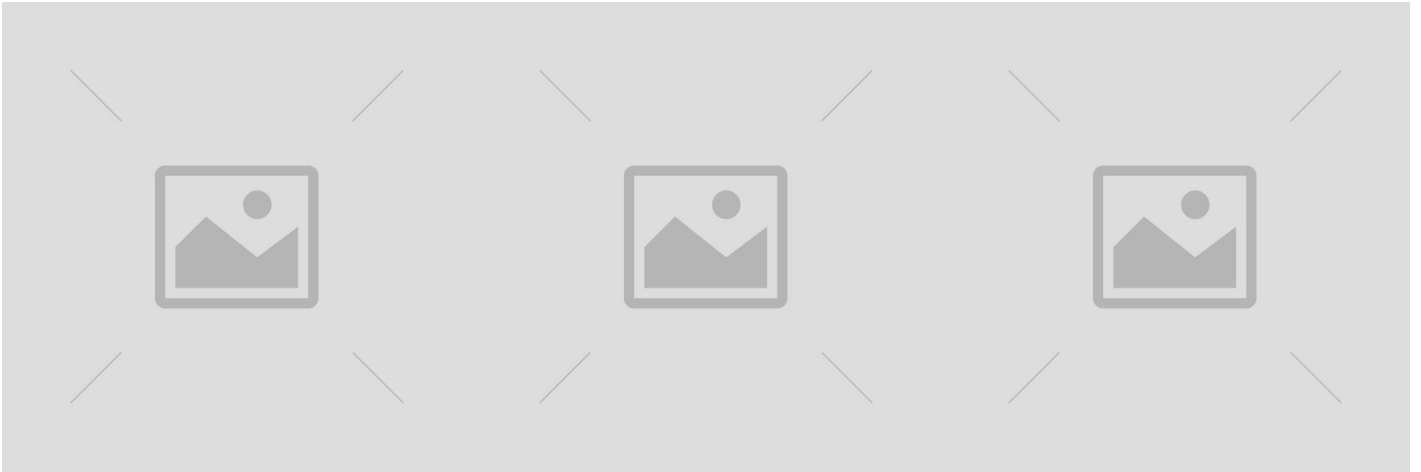

Work Image 4

Work Image 5

Work Image 6

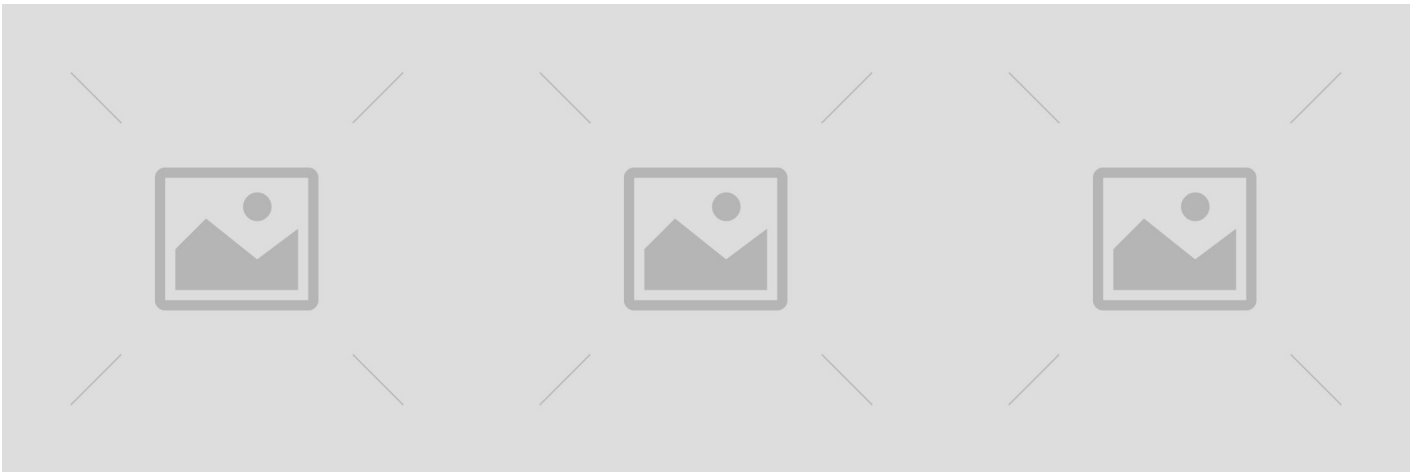


Equipment Locations

Camera Location Image 1

Camera Location Image 2


Camera Location Image 3

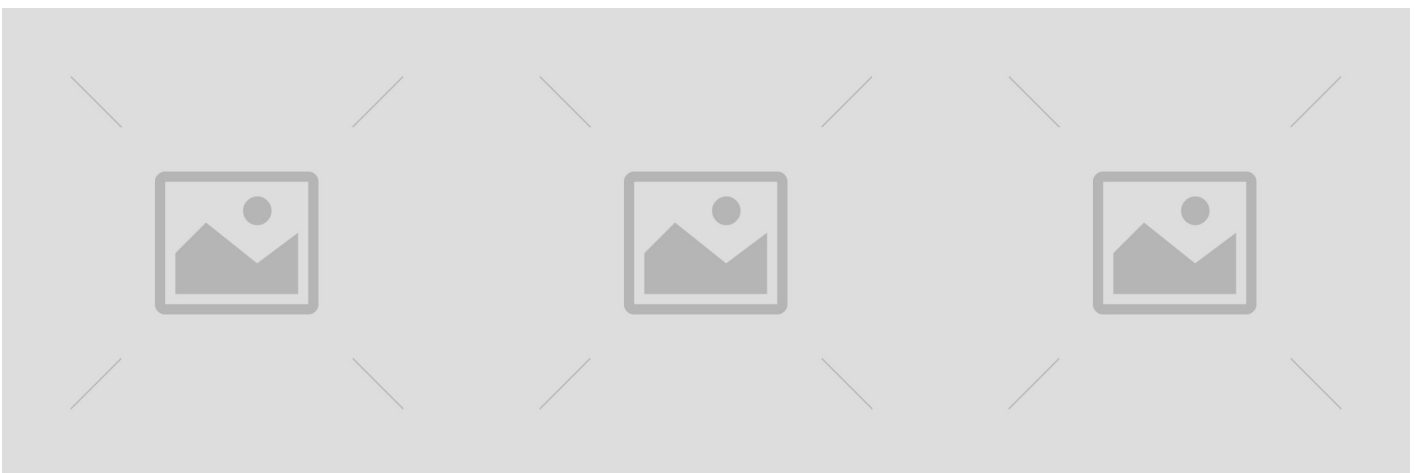

Camera Location Image 4

Camera Location Image 5

Camera Location Image 6

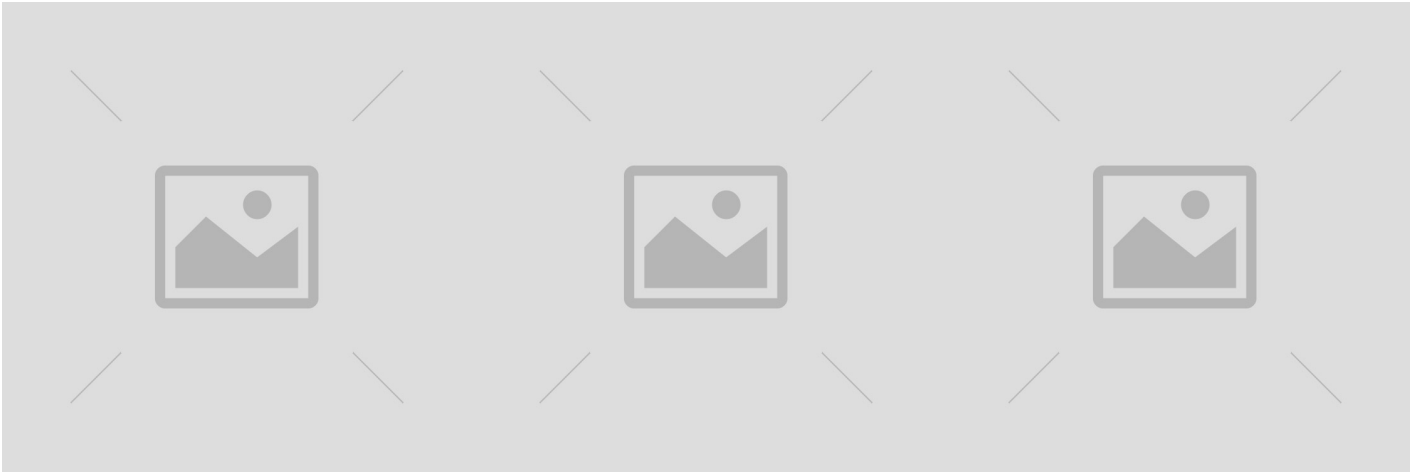

Switch and power location:

Switch and power location image



Recorder location:

Recorder location image



Additional Information:

Audit

CCTV system is installed and programmed per proposal and is operational.: Yes



Camera angles are adjusted and approved by the customer: Yes



Customer is satisfied with cleanliness: Yes

Customer has been trained with camera system including live view, motion detection, and recording retrieval. The customer is satisfied with CCTV customer orientation training: Yes

Customer Name:

.

Customer Signature:
