



Job Sheet

Client site:	Jam box self storage
Site contact:	Aqual
Date of job:	2026-01-05
Days on site:	5
Engineer on site:	Matt / Luke
Type of job:	installation
Number of cameras:	31
Camera locations:	see attached plan


Camera Location Image 1

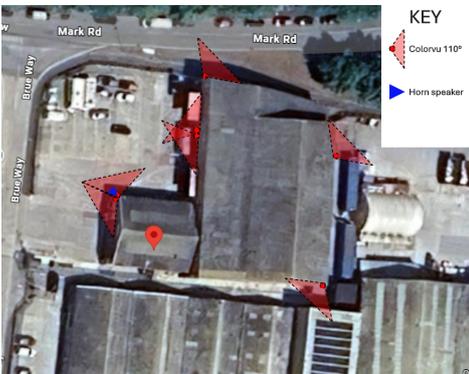

Camera Location Image 2

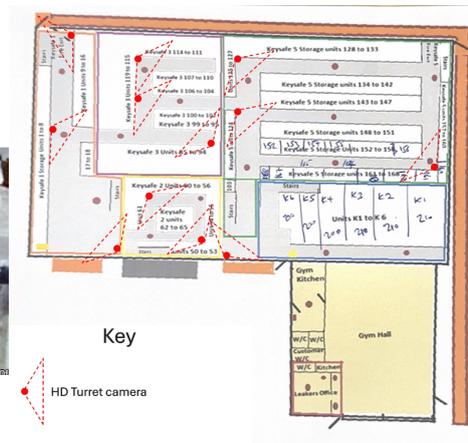

Camera Location Image 3

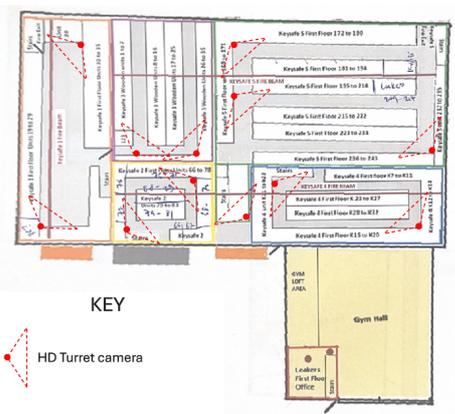

Camera Location Image 4

Camera Location Image 5

Camera Location Image 6



Recorder location:

storage room

Recorder Location Image



Installation instructions:

External There will be seven Hikvision 8MP 4K Hybrid ColorVu and IR Acusense Turrets that will be installed to provide coverage as per the attached plan, The cameras have AI built in and we will utilize this to provide accurate notifications when there are any unwanted visitors on site. The cameras have built in white light technology that enables the cameras to provide a full colour image at night rather than the conventional grey scale images. There will be a horn speaker located externally as per plan and this will enable you to warn off any unwanted visitors, this would be a requirement for the site to be monitored should you wish to go down the monitoring route.

Internal There will be 24 internal cameras that will be HikVision 8MP HD Turret Cameras with a 2.8mm lens and a 40m IR range that will provide coverage of the interior as per plan. There will be a Hikvision HVR 32 channel 16TB with built in acusense that will provide a minimum of 30 days of footage, There will be a 8 port PoE network switch to provide power and data for the IP cameras. The Hikvision HVR 32 channel 16TB with built in acusense will be connected to your broadband and this will enable you to view live footage and playback on the app. All of the equipment will be housed in a lockable data cabinet to keep all of the equipment safe and the cabling will be kept neat and tidy.

Equipment breakdown 24 x HikVision 8MP HD Turret Cameras with a 2.8mm lens and a 40m IR range. 7 x Hikvision 8MP 4K Hybrid ColorVu and IR Acusense Turret. 1 x Hikvision HVR 32 channel 16TB with built in Acusense. 1 x 8 port PoE managed network switch. 31 x Hikvision deep bases. 1 x Horn speaker with a built-in amp. 1 x Lockable data cabinet. 1 x Installation cost including CAT5 cable and electrical sundries. 1 x 12-Month Service and Maintenance Cover. 1 x Warning Signage and CCTV Policy Template. I would anticipate that we can complete the installation of the cameras and commissioning over a 5 day period.

Additional Information:
