


## Job Sheet

Client site:	Storebox Stratford
Site contact:	James / Mark
Date of job:	2026-06-02
Days on site:	3.5
Engineer on site:	Drew / Si
Type of job:	installation
Number of cameras:	13
Camera locations:	as per plan

**Camera Location Image 1**



**Camera Location Image 2**

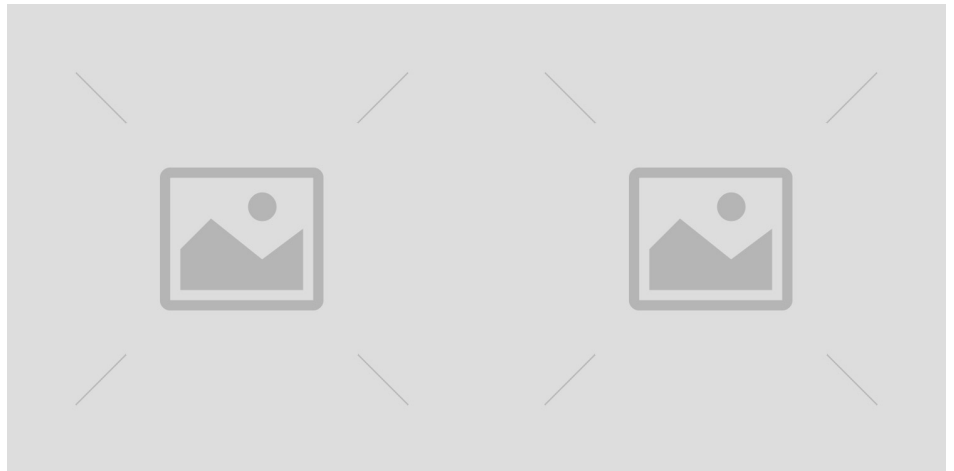

**Camera Location Image 3**

**Camera Location Image 4**

**Camera Location Image 5**

**Camera Location Image 6**



Recorder location:

Office container

**Recorder Location Image**



have put together a proposal for Stratford please see below. There will be two Hikvision 8MP 4K Hybrid ColorVu and IR Acusense Turrets and four Hikvision 8MP 4K Panovu 180 Acusense Turrets mounted on container poles to provide coverage as marked on the plan, The cameras have AI built in and we will utilize this to provide accurate notifications when there are any unwanted visitors on site. We are able to set zones around the site that will trigger the audible and visual outputs on the cameras to deter any unwanted visitors. Both cameras have built in white light technology that enables the cameras to provide a full colour image at night rather than the conventional grey scale images. I have attached a spec sheet for both cameras for you to have a look at and below is a link to a video so you can see the image quality on the Panovu cameras you can jump to 11.50 to save time.

#### Installation instructions:

<https://www.youtube.com/watch?v=VLbtknJqU6g> There will be a Hikvision NVR 16 channel 8TB with built in acusense that will provide a minimum of 30 days of footage, The system will be connected to your router that will enable you to view playback and live images on the app. The cameras will be powered by a 16 port PoE network switch and connected to the NVR We will supply and install 1.2m container poles and mounting brackets to raise the existing cameras up out of reach to reduce the risk of them being tampered with. I have amended the original site plan to ensure you are getting the coverage you require to be able to monitor the site accurately. Equipment breakdown 4 x Hikvision 8MP 4K Panovu 180 Acusense Turret. 2 x Hikvision 8MP 4K Hybrid ColorVu and IR Acusense Turret. 1 x Hikvision NVR 16 channel 8TB with built in Acusense. 6 x Hikvision deep bases. 12 x Container poles. 1 x Installation cost including CAT5 cable and electrical sundries. 1 x 12-Month Service and Maintenance Cover. 1 x Warning Signage and CCTV Policy Template.

Additional Information:

Ensure the system is set up with DSOC and a walk test has been completed, as the site is operational you will need to ensure the site is covered at all times and this site has a track record for being broken into.

---
