Job Sheet

|	
Client site:	Dockweiler
Site contact:	Duncan
Date of job:	2025-08-12
Days on site:	1
Engineer on site:	Matt / Matty
Type of job:	installation
Number of cameras:	8
Camera locations:	External cameras We will install five Hikvision 8MP 4K Hybrid ColorVu and IR Acusense IP Turrets to provide coverage of the external areas marked on the external plan, The cameras have AI built in and we will utilize this to provide accurate notifications when there are any unwanted visitors on site. Both cameras have built in white light technology that enables the cameras to provide a full colour image at night rather than the conventional grey scale images. Internal cameras We will install three Hikvision 8MP 4K IR Acusense IP Turrets to provide coverage of the reception area, toilet area and warehouse.

Camera Location Image 1
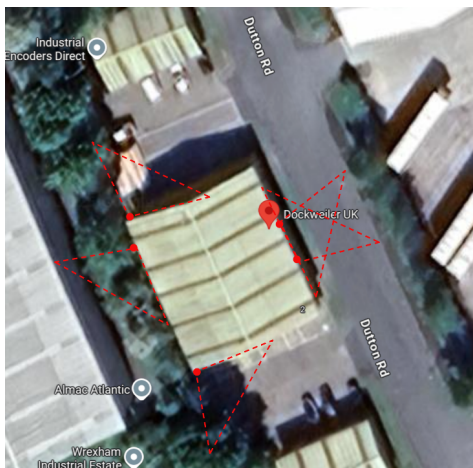
Camera Location Image 2
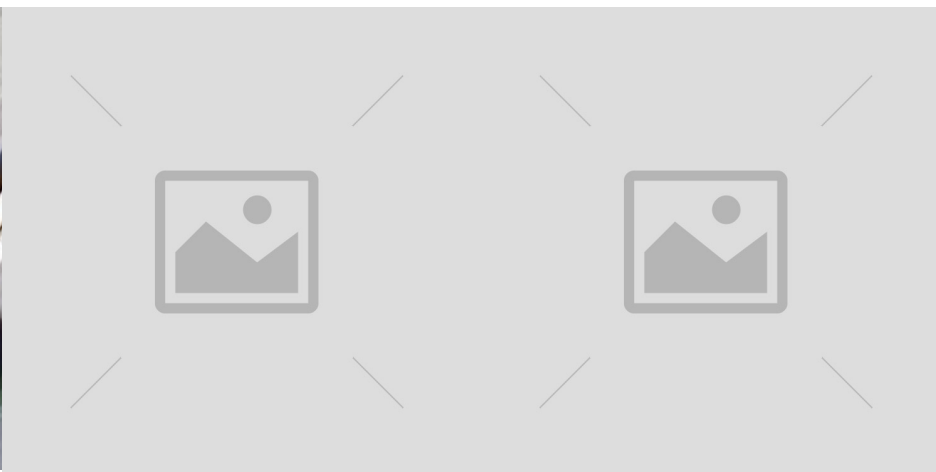
Camera Location Image 3

Camera Location Image 4

Camera Location Image 5

Camera Location Image 6

Recorder location:	Network cab that is located to the rear of the building.

Recorder Location Image

Installation instructions:	External cameras We will install five Hikvision 8MP 4K Hybrid ColorVu and IR Acusense IP Turrets to provide coverage of the external areas marked on the external plan, The cameras have AI built in and we will utilize this to provide accurate notifications when there are any unwanted visitors on site. Both cameras have built in white light technology that enables the cameras to provide a full colour image at night rather than the conventional grey scale images. Internal cameras We will install three Hikvision 8MP 4K IR Acusense IP Turrets to provide coverage of the reception area, toilet area and warehouse. The cameras will be connected to a Hikvision 16-Channel 8MP acusense NVR with a 8TB hard drive that we will connect to your broadband and this will give you the ability to see live view and playback footage on the app. I have gone with a 16 channel NVR to ensure you have space for expansion in the future. Equipment breakdown 5 x Hikvision 8MP 4K Hybrid ColorVu and IR Acusense IP Turrets 3 x Hikvision 8MP 4K IR Acusense IP Turrets 1 x Hikvision 16-Channel 8MP acusense NVR with a 8TB hard drive 1 x 4 Port PoE network switch 1 x 8 Port PoE network switch 1 x Installation cost including CAT5 cable and electrical sundries 1 x 12-Month Service and Maintenance Cover 1 x Warning Signage and CCTV Policy Template
Additional Information:	I would suggest putting a switch near the front of the building that will be used for the two front externals, the reception, the toilet coridor and the camera at the top of the stairs over looking the warehouse.
